Management Presentation Pack · **Internal HRMS Initiative**

PeopleOS — Management Overview

A 12-week internal HR platform for a ~500-employee India IT consultancy, built to own core HR, leave, attendance, documents and approvals — while greytHR stays the system of record for statutory payroll.

Recommendation: Approve with conditions

Audience
CEO, Leadership, HR, Finance, IT

Organization
~500-employee India IT consultancy

Current system
greytHR

MVP scope
India-only

01 Executive Snapshot

Item	Decision
What we are building	Internal Human Resource Management System (PeopleOS)
Primary goal (12 weeks)	Own Core HR, leave, attendance coordination, documents, approvals, ESS/Manager portals

Item	Decision
What we keep external	Indian statutory payroll on greytHR (system of record for payroll)
Team	4 engineers
Initial delivery window	12 weeks / 3 months Fact — hard constraint
Architecture	Modular monolith: NestJS + React + PostgreSQL
Infra — Stage A	Target ₹0 paid cloud (Docker, OSS, free-tier CI)
Infra — Stage B	Azure, after internal validation gates
Long-term option	Multi-tenant SaaS readiness via `tenant_id` — not commercial SaaS in MVP
Management ask	**Approve with conditions**

---

02 What This Product Is About

Purpose

PeopleOS is an owned digital people platform for the company. It becomes the system of record for employee and organization master data, leave and attendance coordination, approval workflows, HR documents, employee and manager self-service, and operational workforce reporting.

It is designed so that, after successful internal use, the same platform can evolve into a commercial multi-tenant SaaS product without a rewrite — while the first 12 weeks deliberately do not fund commercial SaaS features.

The problem it addresses


The company already runs greytHR Fact. Day-to-day friction is believed to remain in manager approvals, attendance corrections, document control, leadership reporting, and process changes that wait on vendor configuration — often spilling into email and Excel Assumption — validate Week 1.

Stakeholder	What hurts today	What PeopleOS targets
Employees	Unclear request status; multi-channel requests	Clear ESS: leave, attendance, documents, status
Managers	Approvals scattered; weak team visibility	Single approvals inbox + team views
HR	Side processes, limited change velocity	Owned workflows, audit, imports
Leadership	Manual headcount/attrition packs	Operational dashboards/reports
Finance	Leave/attendance inputs to payroll need clean handoff	Export/coordination to greytHR payroll
IT	Limited automation/API leverage	Versioned APIs, audit, controlled access

What PeopleOS is — and is not

PeopleOS is	PeopleOS is not (MVP)
Internal HRMS for India IT consultancy (~500 employees)	A greytHR clone
System of record for people, leave, attendance ops, docs, approvals	A full Indian statutory payroll/tax engine
Modular monolith ready for later Azure and SaaS	Microservices / Kubernetes Day 1
UX- and workflow-focused product	An AI-agent platform Day 1
Compatible with keeping greytHR for payroll	A forced rip-and-replace of payroll in 12 weeks

Relationship to greytHR



Domain	System of record (MVP)
Employee master, org structure	**PeopleOS** (after migration)
Leave / attendance coordination	**PeopleOS**
Documents / approvals / ESS	**PeopleOS**
Statutory payroll, payslips, PF/ESI/TDS filings	**greytHR**

> **STRATEGIC HONESTY FOR MANAGEMENT**
>
> If the only objective were to run India payroll reliably, continuing greytHR alone can be rational. Building PeopleOS is justified by ownership, fit, UX/workflow control, APIs, auditability, and future product optionality — not by beating greytHR at compliance payroll in three months.

---

03 Development Architecture

Architecture style

Decision (locked): Modular monolith — one NestJS application with clear domain modules, one React SPA, one PostgreSQL database.


Choose	Avoid (MVP)
Modular monolith	Microservices
Docker Compose locally	AKS / Kubernetes
Shared schema + `tenant_id`	Database-per-tenant Day 1
Provider interfaces for auth/files	Hard Azure-only lock-in in core domain

Technology stack

Layer	Technology	Cost class (Stage A)
Frontend	React + TypeScript + Vite	Open source
Backend	NestJS + TypeScript	Open source
ORM / migrations	Prisma	Open source
Database	PostgreSQL 16	Open source (Docker)
API contract	OpenAPI / Swagger	Open source
Authentication	Local email/password + JWT access/refresh; MFA-ready	Open source
Authorization	RBAC + resource rules (self / manager chain / HR)	Built in-product
File storage	Local filesystem or MinIO	Open source
Email (dev)	Mailpit; company SMTP for pilot	OSS / existing
Cache (optional)	Redis	Open source
Containers	Docker + Docker Compose	OSS — verify Desktop licensing with IT

Layer	Technology	Cost class (Stage A)
CI/CD	GitHub Actions	Free tier — quota-limited, not unlimited
Logging	Structured JSON logs (e.g. pino)	Open source
E2E testing	Playwright	Open source

Logical view

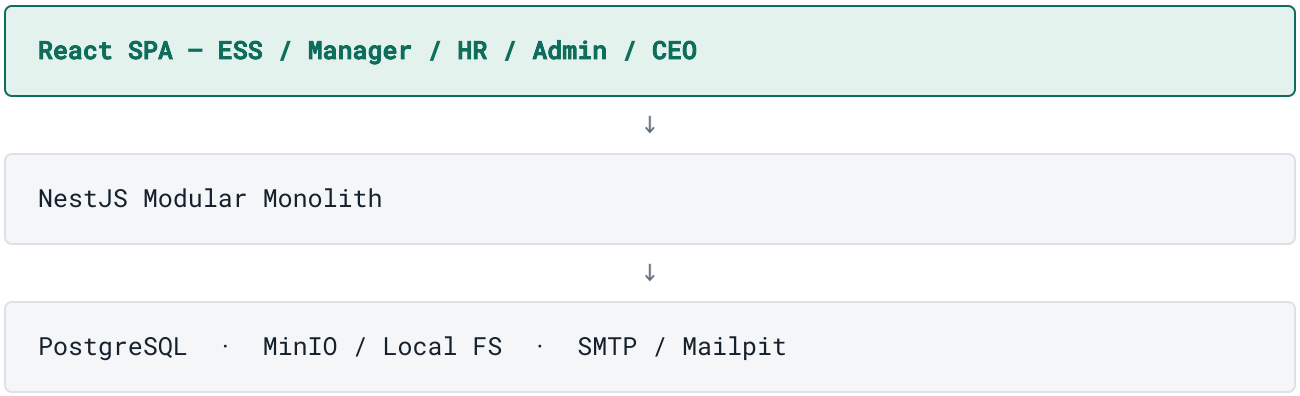

Module boundaries: Identity · Core HR · Leave · Attendance · Workflow · Documents · Notifications · Reporting · Admin · Payroll integration (export only).

Stage A vs Stage B infrastructure

Concern	Stage A — Development / Pilot	Stage B — Azure production (after gates)
Compute	Developer machines + optional internal VM	Azure Container Apps (preferred over AKS)
Database	PostgreSQL in Docker	Azure Database for PostgreSQL Flexible Server
Files	Local / MinIO	Azure Blob Storage (private)
Identity	Local JWT	Microsoft Entra ID (OIDC SSO)
Secrets	`.env` (git-ignored)	Azure Key Vault

Concern	Stage A — Development / Pilot	Stage B — Azure production (after gates)
Messaging	In-process events + outbox	Azure Service Bus when volume justifies
Monitoring	Structured logs (+ optional local Grafana)	Azure Monitor / Application Insights
Cash target	**₹0 paid cloud** wherever reasonable	Funded only after UAT + adoption gates

> **FACT**
>
> Free tiers such as GitHub Actions minutes have limits. Exceeding quotas can block CI or require payment — plan self-hosted runners or throttled pipelines.

Security and tenancy (management view)

Topic	Approach
Data sensitivity	HRMS holds PII and documents — security is first-class
Access control	Roles: Employee, Manager, HR, Admin, CEO (read dashboards)
Audit	Immutable audit events for sensitive actions
Multi-tenancy readiness	`tenant_id` on tenant-scoped tables from Day 1; single company tenant in MVP
Payroll data	Prefer not storing full payslip/statutory payroll in PeopleOS while greytHR remains payroll SoR

---

04 Features

P0 Committed for the 12-week MVP

Area	Capabilities
Identity & access	Login, roles/permissions, session security, MFA-ready design
Core HR	Org units, departments, designations, locations, employee profiles, manager hierarchy, employment status, search
Leave	Policies/types, balances, apply/approve/reject, holidays, balance visibility in ESS
Attendance	Daily mark, CSV import hook (biometric export bridge), correction requests with approval, team views
Workflow engine v1	Sequential stages; role or reporting-manager approvers; unified inbox; reminders (escalation is P1)
Documents	Upload, version metadata, access control, audited download
ESS	Employee home: leave, attendance, docs, notifications
Manager portal	Approvals inbox, team leave/attendance
Notifications	In-app + email on submit/approve/reject
Audit	Searchable audit log for sensitive actions
Reports	Headcount, leave utilization, attendance summary, basic attrition
Migration	greytHR-oriented CSV/Excel import + reconciliation report
Platform	Docker Compose stack, OpenAPI, CI pipeline, structured logging

P1 Stretch — not promised

Feature	Why valuable
Light ATS (requisition → candidate → status → offer draft)	Hiring visibility
Onboarding checklists	IT consultancy joiners

Feature	Why valuable
IT asset assignment (laptops)	High operational value for services firms
Simple HR helpdesk tickets	Reduce email chaos
Workflow escalation / delegation	Hardens approvals under load

P2 Deferred — will not build in MVP

- Full Indian statutory payroll engine (PF/ESI/PT/TDS/challans/Form 16 automation)
- Performance / OKR suite, LMS, expenses engine
- Native mobile apps, WhatsApp bots
- AI agents / copilots as a product bet
- Multi-country HR, commercial billing, SCIM marketplace
- AKS / microservices "for enterprise optics"
- Full biometric device cloud

---

05 Team Members Required and Timeline

Core delivery team — 4 engineers

Role	Primary ownership
Lead Developer / Solution Architect	Architecture, ADRs, security baseline, critical reviews, stakeholder interface, scope control
Backend Engineer	NestJS modules, PostgreSQL/Prisma, workflow engine, APIs, integrations/exports
Frontend Engineer	React ESS / Manager / HR / Admin experiences, accessibility, UX fidelity

Role	Primary ownership
Full-stack / QA Automation	CI/CD, Docker, E2E/API tests, migration scripts, pilot deploy/ops

No dedicated Product Manager in the four — Lead and HR Head/HR Executive share requirements and UAT ownership Assumption

Essential non-engineering stakeholders

Role	Involvement
HR Head	Process owner, UAT sign-off, policy decisions
HR Executive	Day-to-day UAT, data cleansing, training support
Finance	Payroll handoff validation; cost baseline of current greytHR
IT	SMTP, pilot host VM, identity/email standards
CEO / sponsor	Go/No-Go, condition enforcement, Azure Phase 2 gate

Capacity model Estimate

Item	Value
Gross capacity	4 × 12 × 5 = **240 person-days**
Non-coding overhead (meetings, reviews, testing, docs, bugs)	~35–40%
Effective build capacity	**~145–155 person-days**
Contingency	~15% → **~127 commit-able** person-days for P0

This is why P0 is brutal and P1 is stretch-only.

Twelve-week delivery timeline

Weeks	Focus	Outcome
1–2	Discovery, PRD freeze, UX wireframes, ADRs, schema v1, greytHR export discovery	Scope locked
3–4	Foundation: auth, RBAC, audit, Docker, CI, migrations	Platform runnable
5–7	Core HR + Leave + Workflow engine	Core lifecycle working
8	Attendance + corrections + holidays	Attendance path live
9–10	ESS/Manager, Documents, Notifications, Reports	End-user portals usable
11	Security hardening, HR UAT, performance smoke, migration dry-run	Go/No-Go ready
12	Pilot go-live (subset of users), training, runbooks, KPI baseline	Controlled production pilot

CRITICAL PATH


Requirements freeze → Auth/RBAC → Employee master → Leave + Workflow → ESS approvals → Migration dry-run → Pilot. A slip on leave/workflow endangers the date.

Sprint shape: 2-week sprints (Sprint 0 discovery through Sprint 6 pilot). Weekly demos to HR Head; scope changes require written trade-offs against P0.

---

06 Phasewise Timeline Roadmap

The horizon below mixes the 12-week MVP with the 12–24 month product roadmap. Phase durations outside the 12-week window are estimates, not contracts Estimate.



Months 0–3

Phase 1 — Internal HRMS MVP

Objective Ship P0; employees/managers/HR run leave, attendance, core HR, documents, approvals on PeopleOS

Environment Stage A: Docker / OSS / free-tier CI; pilot on existing company VM preferred

Payroll Remains on greytHR

Exit criteria UAT signed; migration dry-run accepted; no Sev-1 authz/data leaks; payroll export path works; pilot cohort live

Months ~3–9

Estimate

Phase 2 — Enterprise hardening & production Azure

Objective Company-wide rollout readiness; production-trustworthy ops

Build Azure Container Apps + Azure PostgreSQL + Blob + Key Vault + Monitor; MFA for privileged roles; backup/restore drills; stronger workflows (delegation/escalation); richer reports; selected P1 (e.g. assets)

Still not External multi-tenant billing, marketplace, AI platform bet

Exit criteria Security baseline signed; runbooks exist; Azure (or approved prod) RPO/RTO agreed; adoption metrics reviewed

Months ~9–14

Estimate

Phase 3 — SaaS foundation

Objective Technical multi-tenant readiness for possible commercialization

Build Enforce tenant isolation tests; feature flags; admin APIs; webhook groundwork; SSO packaging design

Still not Self-serve signup + billing as a forced MVP of SaaS

Months ~14–20

Estimate

Phase 4 — Commercial SaaS

Objective External customers only after internal proof

Build Tenant onboarding, subscription/billing, commercial SLAs, partner payroll integrations, support model

Gate Separate investment case — not automatic

Months ~20–24+

Estimate

Phase 5 — Advanced platform

Examples Advanced analytics, localization depth, marketplace, carefully validated AI assistance

Rule Fund only with evidence of demand and data quality

Production path (simplified)

Stage	Where it runs	When
Development	Local Docker Compose	Weeks 1–11
Pilot production	Existing org VM / controlled host	Week 12
Enterprise production	Azure (Stage B)	After Phase 1 exit + budget approval
Multi-tenant SaaS production	Azure hardened + tenancy ops	Phase 4+

---

07 Future Updates

Near-term — immediately after MVP, if capacity/priority allows

1. Workflow escalation and delegation
2. IT asset tracking
3. Onboarding checklists
4. Light recruitment pipeline
5. HR helpdesk tickets

6. Stronger reporting packs for CEO/HR

Medium-term — hardening / Azure

1. Entra ID SSO and stronger MFA policy
2. Azure managed database, blob, monitoring, Key Vault
3. Improved backup/DR drills
4. Deeper greytHR (or successor) payroll integration automation
5. Document retention and e-sign integration — integrate, don't build

Long-term — SaaS optionality

1. True multi-tenant commercial operations
2. Billing and subscriptions — only when commercializing
3. Public developer APIs / webhooks
4. Custom fields and branding for tenants
5. Regional compliance packs beyond a single India entity

What management should not fund early

Premature investment	Why wait
Full payroll engine	High complexity/compliance; greytHR already strong
AI agents as headline	Needs clean data + stable workflows first
Microservices / AKS	Ops cost exceeds benefit for a 4-person team at ~500 users
Billing / marketplace	Distracts from internal adoption proof
Native mobile + WhatsApp Day 1	Responsive web covers MVP; native is a later product line

---

08 Management Ask / Recommendation

Approve with conditions

Conditions — non-negotiable

1. **P0 scope freeze** as listed in Section 4; P1 only with Lead confirmation of spare capacity.
2. **No statutory payroll engine** in the 12-week program.
3. **greytHR remains payroll system of record** until an explicit Phase 2 decision.
4. **Azure spend gated** on UAT pass + pilot adoption thresholds, defined in Weeks 1–2.
5. **Security review + backup/restore drill** before company-wide rollout.
6. **Weekly demos** to HR Head; scope changes require written trade-offs.
7. **Success metrics baselined** in Weeks 1–2; 90-day review with CEO.

Metrics to measure

no invented ROI

Area	Metric to measure
Adoption	% employees monthly active on ESS
Self-service	% leave requests in-system (not email)
Speed	Median leave approval time

Area	Metric to measure
HR load	Hours/week on Excel consolidations / corrections
Quality	% employees with complete mandatory profile fields
Trust	Sensitive actions with audit events; Sev-1 incidents
Leadership	Time to produce monthly headcount/attrition pack

IF CONDITIONS ARE REJECTED

Do not approve a full platform build. Instead run a short discovery and buy/switch evaluation — deepen greytHR vs. alternatives — without engineering a new system of record.

---

09 Appendix — Where to Read More

Full CEO approval pack	01-executive-proposal.md
Market and competitive logic	02-market-analysis.md
Product vision	03-product-vision.md
Detailed MVP PRD	05-product-requirements-mvp.md
System architecture	10-system-architecture.md
Zero-cost stack	18-zero-cost-architecture.md
Azure target	19-azure-target-architecture.md
12-week plan / team R&R	24-project-plan-12-weeks.md

Sprint plan	25-sprint-plan.md
Risks	23-risk-register.md
SaaS roadmap	28-saas-roadmap.md
Final decisions A–L	appendices/part-48-final-recommendation.md
Doc index	00-README.md
Quick-share artifact	../artifacts/31-management-overview/brief.html

---

Document control — synthesized from the PeopleOS enterprise blueprint. Locked decisions above must not be reopened casually during the 12-week program.
